

ATLANTIC YARDS CONSTRUCTION UPDATE
Weeks of December 7, 2009 through December 14, 2009

In an effort to keep the Atlantic Yards Community aware of upcoming construction activities, ESD and Forest City Ratner provide the following outline of anticipated upcoming construction activities.

Please note: the scope and nature of activities are subject to change based upon field conditions. In addition, during the utility work water shut offs may be required; these shut downs are done under the oversight of DEP and property owners will be given advance notice. All work has been approved by appropriate City and State agencies where required. In addition to the activities described below noise attenuation and vibration monitoring measures are underway in connection with the Memorandum of Environmental Commitments dated 12/08/06.

If you have any questions please feel free to contact our project Ombudsperson at: 212-803-3233 or AtlanticYards@empire.state.ny.us

Long Island Rail Road/Vanderbilt Yard Work

- Installation of Lighting
- Completion of Temp Yard Punch list
- Removal of old Track in BL1119 and BL1120
- Relocation of the MG Set from BL1119 to BL 1120
- Installation of a new Access Road in BL1120
- Work is anticipated to continue through the end of the year.

Environmental Remediation

- The environmental consultant will begin shallow excavation and drilling to test and classify soils in blocks 1127 and 1119. Work will continue on these blocks and 1118 for 3 months. This is prep work required in advance of any actual removal of soil from the site.

Infrastructure


- Infrastructure work related to installation of new sewer chambers at the intersection of 6th Avenue at Pacific Street is complete. Infrastructure work related to the installation of new a water main along the east side of Flatbush Avenue is complete.
- The traffic and pedestrian safety barriers along the north side of Flatbush Avenue and Block 1118 for sewer installation is complete for the current phase of the work. Additional protection will be installed to modify traffic in 5th Avenue upon approval from the Department of Transportation.
- The contractor continues to conduct pile drilling, excavation work, and pipe and chamber installation on Blocks 1127 and 1118 in connection with sewer installation. Work will continue for 5 to 6 months.

- During the course of this work, the contractor may encounter unforeseen contaminants, underground storage tanks or other structures. In the event that this happens and where appropriate, notification will be given to the DEC and remediation steps were implemented.

Demolition

- The Abatement contractor began installation of scaffolding in preparation for the removal of asbestos at the roof at 475 Dean Street.
- The Abatement and Demolition contractor will install sidewalk protection as required by the Department of Buildings in preparation for the removal of asbestos and demolition of 648 Pacific Street. The start of this work is dependent upon approvals by the Department of Buildings.
- The Abatement contractor will install sidewalk protection as required by the Department of Buildings in preparation for the removal of asbestos and demolition of 467 Dean Street. The start of this work is dependent upon approvals by the Department of Buildings.

Atlantic Yards Public Utility Infrastructure

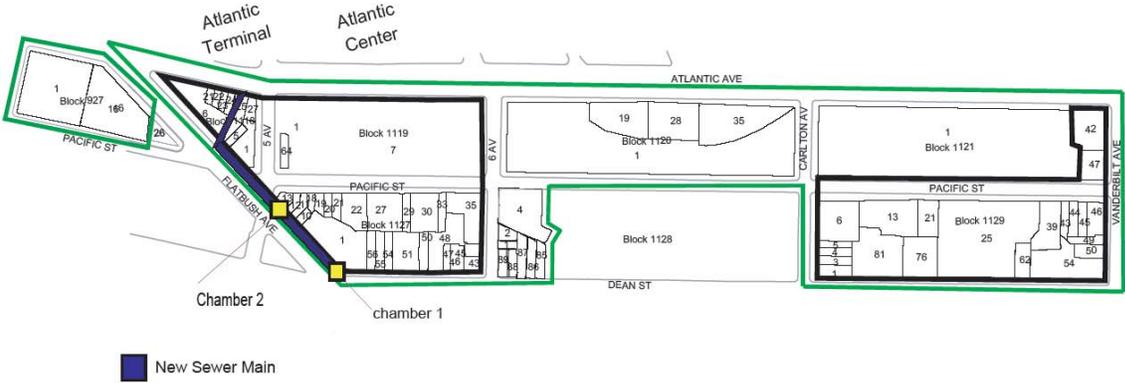

Atlantic Yards Demolition Status

