

ATLANTIC YARDS CONSTRUCTION UPDATE
Weeks of March 29, 2010 and April 5, 2010

In an effort to keep the Atlantic Yards Community aware of upcoming construction activities, ESD and Forest City Ratner provide the following outline of anticipated upcoming construction activities.

Please note: the scope and nature of activities are subject to change based upon field conditions. In addition, during the utility work water shut offs may be required; these shut downs are done under the oversight of DEP and property owners will be given advance notice. All work has been approved by appropriate City and State agencies where required. In addition to the activities described below noise attenuation and vibration monitoring measures are underway in connection with the Amended Memorandum of Environmental Commitments dated as of 12/21/09.

If you have any questions please feel free to contact our project Ombudsperson at: 212-803-3233 or AtlanticYards@empire.state.ny.us

Long Island Rail Road/Vanderbilt Yard Work

- Lighting installation has been completed. LIRR will operate Low-intensity lights within the rail yard will begin continuous nightly operation; Pole-mounted Flood Lights will typically be used during emergencies or special night-time work.
- Continue to complete minor items remaining on Temp Yard Punch list.
- Work continues on the relocation of the MG Set from BL1119 to BL 1120. Work entails mechanical and electrical work inside the building.
- Installation of protection of LIRR substation A0-1 via erection of a sidewalk bridge over this equipment in BL1119 continues
- Jersey Barriers and fencing to separate the LIRR Yard and facilities from the Arena construction area will be installed on Block 1119.
- Demolition of the former MG Set building close to the Fifth Avenue end of the site will commence.
- Work will begin on installation of a Construction Site Office Trailer Park and Site Logistics Area in BL1129

Environmental Remediation

- The environmental consultant has completed most of the shallow excavation and drilling to test and classify soils in blocks 1127 and 1119. Work will continue on parcels that were previously blocked with utility construction vehicles. This is prep work required in advance of any actual removal of soil from the site.
- Continuation of water quality monitoring around the site per NYS Department of Environmental Conservation requirements.

In accordance with the request of the NYS Department of Environmental Conservation, additional monitoring wells are being installed on block 1118 lots 1 and block 1119 lots 1 & 64 and Block 1127, lots 11, 12, and 13.

Infrastructure

- The contractor completed pile drilling in all areas including 5th Avenue/Flatbush intersection. Sewer pipe installation along Flatbush has resumed
- The contractor continues to perform ancillary work at the recently installed sewer pipe between Flatbush and Atlantic. Underpinning of subway vent structure and demolition of TA manhole has been completed. Including underpinning a section of the subway vent structure and demolition of a TA manhole.
- Contractor continues work in Atlantic Avenue related to the cut and cap an abandoned water main. The work at the location west of Flatbush is being performed at night and will be plated over every morning before rush hour traffic begins, per DOT stipulations. The location at the east is being performed during regular work hours behind barricades that will remain in place until work is completed.
- Immediately following the water main cut and cap, the contractor will dig test pits on Atlantic Avenue between Flatbush and 6th Avenue to locate the exact profile of the LIRR tunnel and existing sewer pipes -- this work has been delayed due to field conditions. The work will be performed with the approval of the LIRR.
- Full MPT along Atlantic Avenue between Flatbush Avenue and 5th Avenue has been installed. Contractor is installing plywood fencing above concrete jersey barriers. The fencing and barriers do not exceed 8' in height.

The contractor continues installation of water main crossing BL 1118.

- During the course of this work, the contractor may encounter unforeseen contaminants, underground storage tanks or other structures. In the event that this

happens and where appropriate, notification will be given to the DEC and remediation steps were implemented.

Demolition

- The abatement is complete at 624 and 648 Pacific Street and 473 and 475 Dean Street. Filings for demolition permits are in progress.
- Sidewalk sheds and scaffolding were installed at 648 Pacific Street and 467 Dean Streets as required by the Department of buildings. The DOB will not require a shed at 624 Pacific Street because a fence will be erected around the building with enough buffer to make a shed unnecessary.
- A fence will be erected along the centerline of Pacific Street between 6th Avenue on the east and the perimeter of the demolition buffer of 624 Pacific Street on the west. The fence will allow unobstructed pedestrian and vehicular passage along the south half of the street from 6th Avenue to 636 Pacific Street and will prevent those vehicles and pedestrians from entering the construction zone at the north and west parts of the street.
- As site control is granted, abatement filings will be submitted on additional buildings in the arena footprint and on Block 1129.
- Demolition of 467 and 475 Dean Street and 624 and 648 Pacific Street is expected to begin within the two week period.


Arena

- Hunt will continue enclosing the construction site on Block 1119 and the northern half of Pacific Street between 5th and 6th Avenues, by installing a combination of chain-link, and plywood fencing on jersey barriers, according to the requirements of DOT, DOB and the Memo of Environmental Commitments. Local and Emergency Access for the resident at 636 Pacific Street will be maintained.
- Upon completion of site enclosure, including inspections by DOB, Hunt will begin mobilization of equipment (pile drillers, excavation vehicles and trailers).
- Prior to their work on site, workers undergo Site safety and mitigation orientation.
- Upon approval of necessary DOB permit, drilling activities will commence.

Full Street Closures

The new traffic flow, implemented as of March 8, 2010, continues to be monitored by the DOT and private transportation consultants. As requested by DOT, NYPD, FDNY, the LIRR or other agencies, slight modifications have been implemented to correct unforeseen problems or improve flow.

Atlantic Yards Public Utility Infrastructure

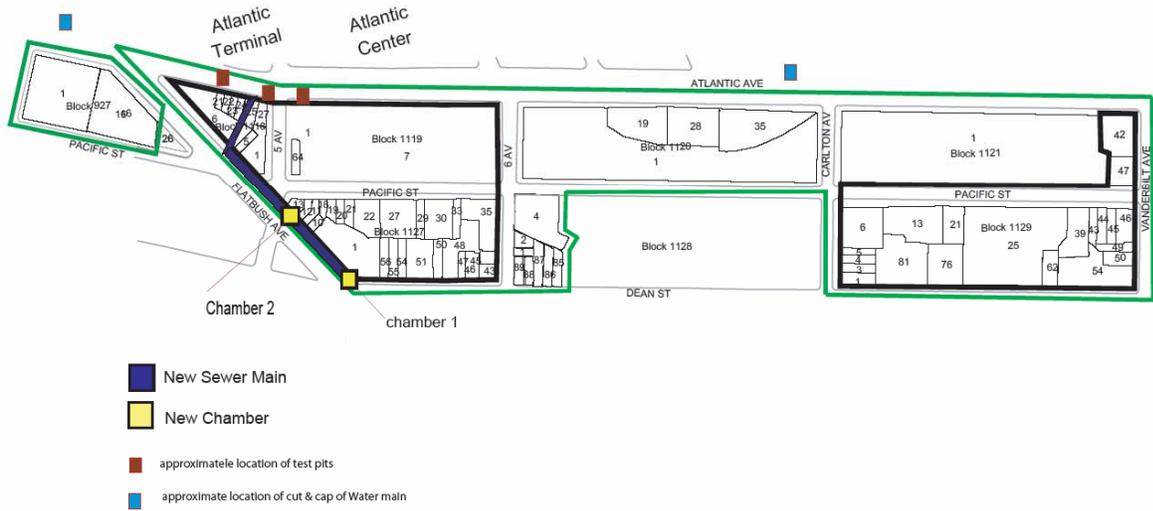

as of February 15, 2010

Atlantic Yards Demolition Status

