


PACIFIC PARK BROOKLYN

Truck Protocols

1. Trucks are required to use NYCDOT-designated truck routes for traveling to and from the construction site, which include primarily Atlantic Avenue, Flatbush Avenue, 4th Avenue and the Brooklyn-Queens Expressway, except as required for movement between the staging and construction areas;
2. Routing map to the site, along with DOT truck route map, is attached (the DOT truck route map can also be obtained from <http://www.nyc.gov/html/dot/html/motorist/trucks.shtml#routes>);
3. Trucks shall use the Pacific Street Queue Area or other designated location for truck marshalling and queuing to the extent practicable and appropriate;
4. Limiting on-site speed to five miles per hour;
5. Idling of vehicles and non-road engines for more than three minutes is prohibited per New York City law, except when operation of the engine is required to operate ancillary truck-mounted equipment (e.g. , concrete trucks);
6. Covering all trucks carrying loose material such as debris, excavate or fill, and verifying that covers on all such trucks have been properly sealed. Outgoing trucks shall be inspected by the contractor at the gate, and not allowed to exit if covers are not properly sealed;
7. Washing the wheels of all trucks as they exit from the site;
8. Truck deliveries will be scheduled and untimely deliveries shall be turned away or reassigned with different delivery times;
9. Curbside deliveries shall occur within delineated closed-off area;
10. Designated onsite staging areas will be maintained throughout construction to store materials and accommodate construction vehicles that require early arrival and marshaling for immediate material delivery to high-demand construction areas.

FAILURE TO COMPLY WITH THESE REQUIREMENTS WILL RESULT IN THE NON-COMPLIANT DRIVER, AND AND/OR FIRM, BEING DENIED ACCESS TO THE SITE FOR THE DURATION OF THE PROJECT

Truck Route for B14 Project
Ingress Map Via Carlton (Primary Route)

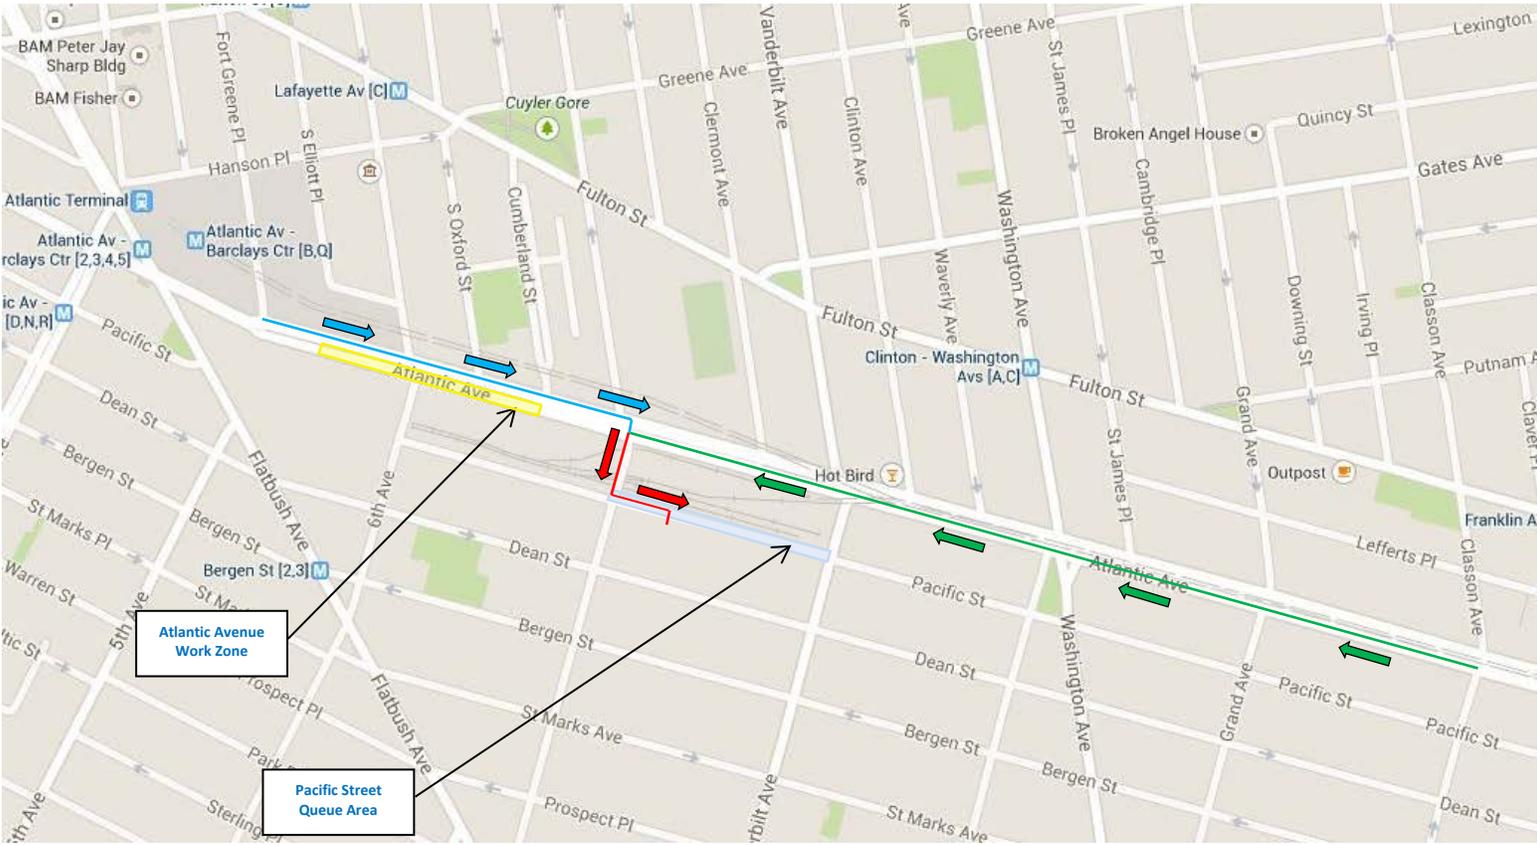

Option 1 - Traveling East on Atlantic Avenue

- 1. Travel east on Atlantic Avenue.
- 2. Turn right onto Carlton Avenue.
- 3. Turn left onto Pacific Street.
- 4. Turn right into B14 Site.


Option 2 - Traveling West on Atlantic Avenue

- 1. Travel west on Atlantic Avenue.
- 2. Turn left onto Carlton Avenue.
- 3. Turn left onto Pacific Street.
- 4. Turn right into B14 Site.

Legend

-  Common Ingress route
-  Ingress route from Atlantic Avenue (Heading East)
-  Ingress route from Atlantic Avenue (Heading West)

Truck Route for B14 Project
Ingress Map Via Vanderbilt (Secondary Route)

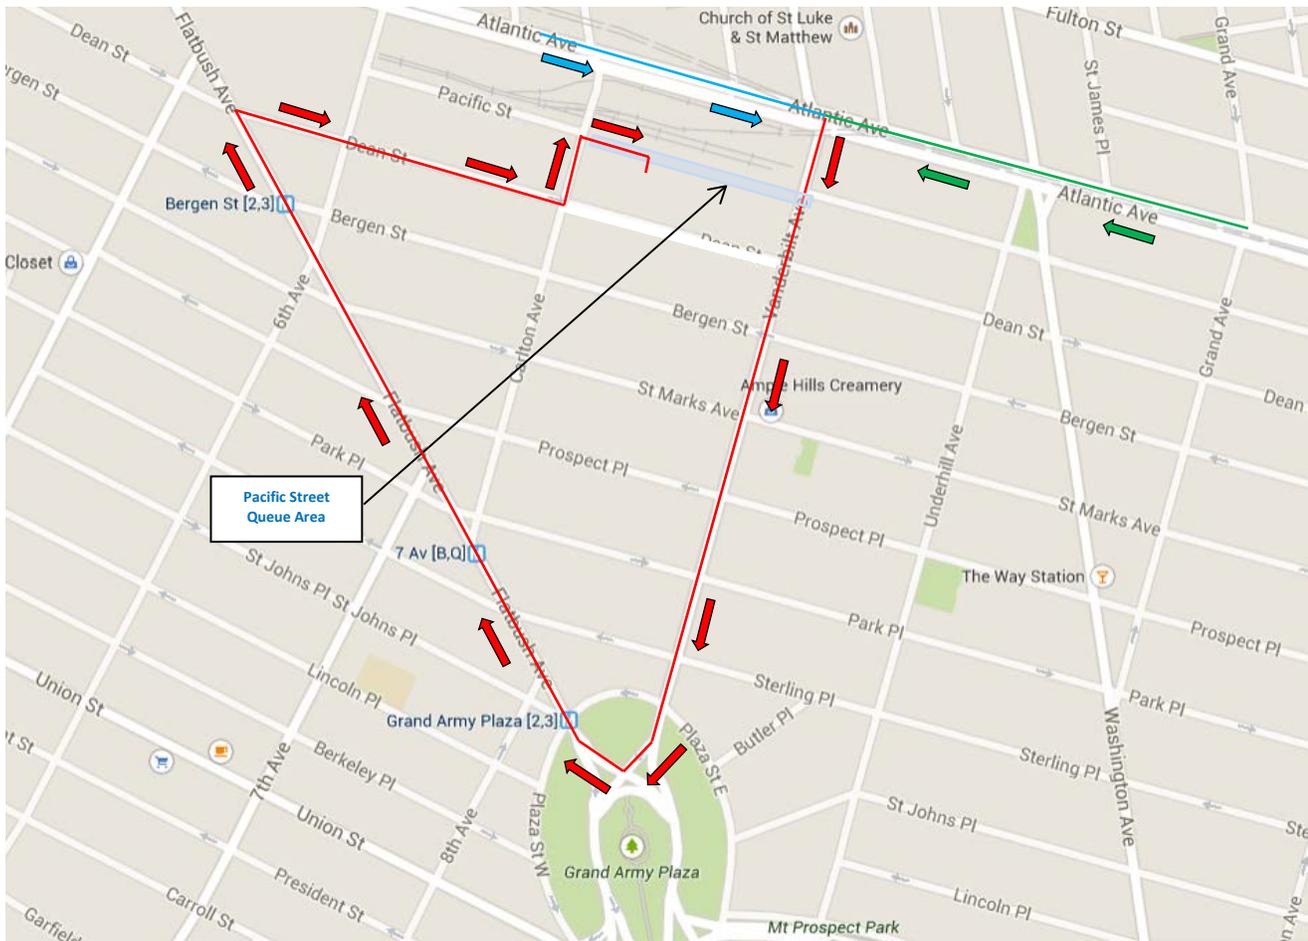

Option 1 – Travel West on Atlantic Avenue to B14 Site

1. Turn left onto Vanderbilt Avenue.
2. Turn right onto Flatbush Avenue at Grand Army Plaza.
3. Turn right onto Dean Street.
4. Turn left onto Carlton Avenue.
5. Turn right onto Pacific Street.
6. Turn right into Site.


Option 2 – Travel East on Atlantic Avenue to B14 Site

1. Turn right onto Vanderbilt Avenue.
2. Turn right onto Flatbush Avenue at Grand Army Plaza.
3. Turn right onto Dean Street.
4. Turn left onto Carlton Avenue.
5. Turn right onto Pacific Street.
6. Turn right into Site.

Legend

-  Common Ingress route
-  Ingress route from Atlantic Avenue (Heading East)
-  Ingress route from Atlantic Avenue (Heading West)

Truck Route for B14 Project
Egress Map Via Carlton

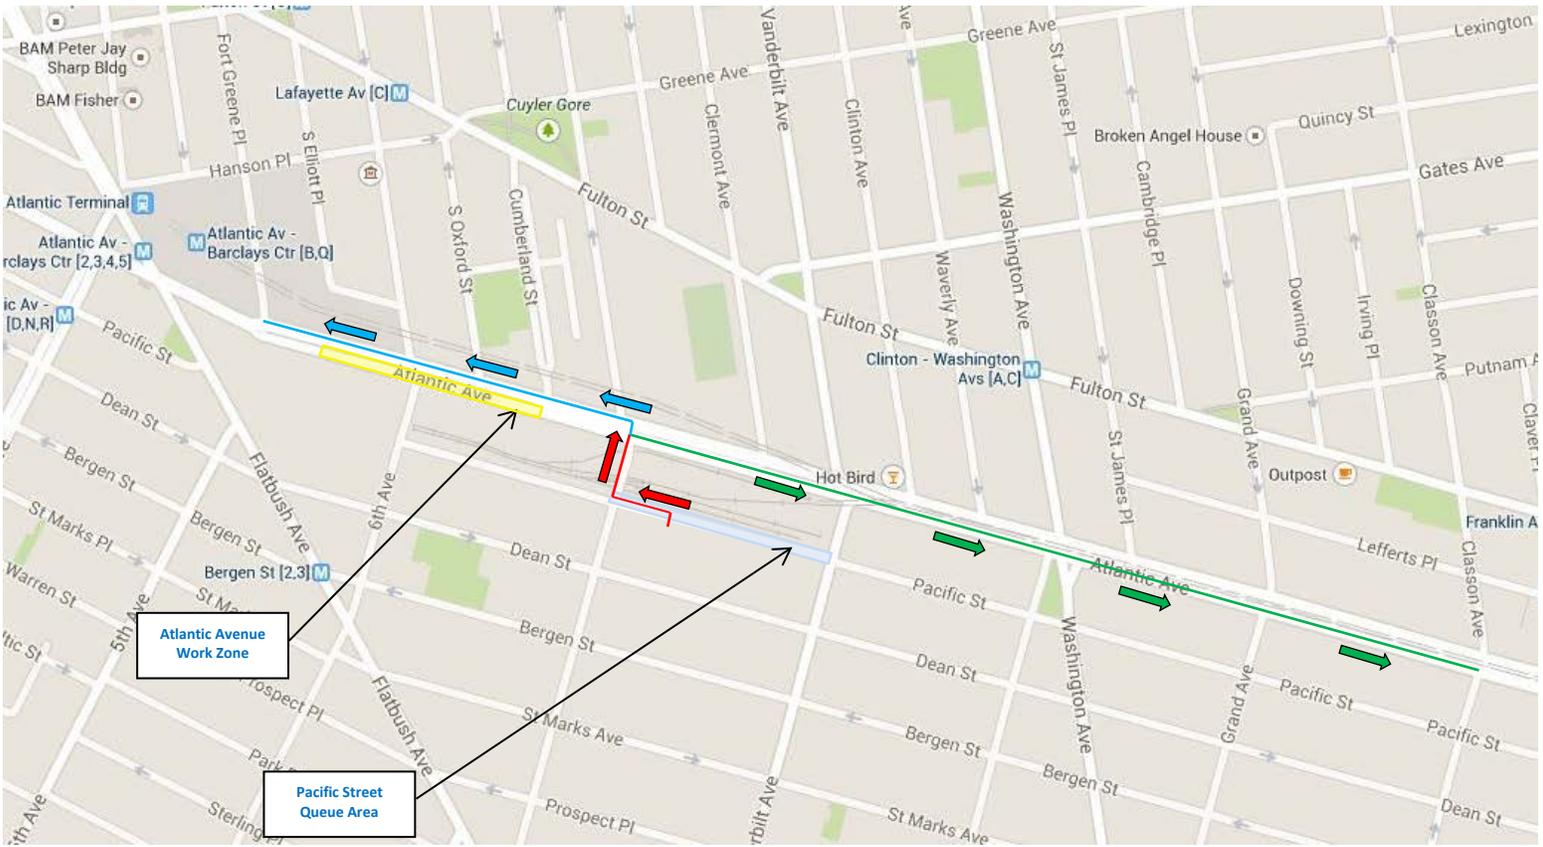

Exit via Carlton Avenue

1. Exit the job site and head west on Pacific Street.
2. Turn right onto Carlton Avenue.
3. Turn left or right onto Atlantic Avenue and travel on approved NYCDOT-designated truck routes.

Legend

- ➔ Common Egress route
- ➔ Egress route to Atlantic Avenue (Heading West)
- ➔ Egress route to Atlantic Avenue (Heading East)

Key

- Local Truck Routes
- Through Truck Routes
- Project Site Location

